
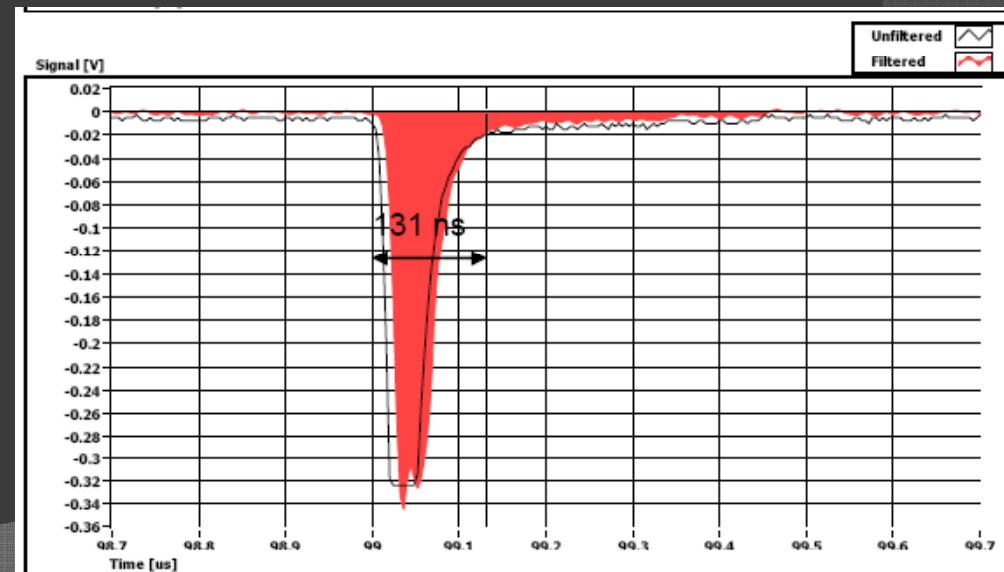


EA section meeting, 31st August 2007

MERIT STATUS

Beam test 24th Aug. 07

- First proton beam successfully extracted to MERIT beam branch
- Particle detectors operational


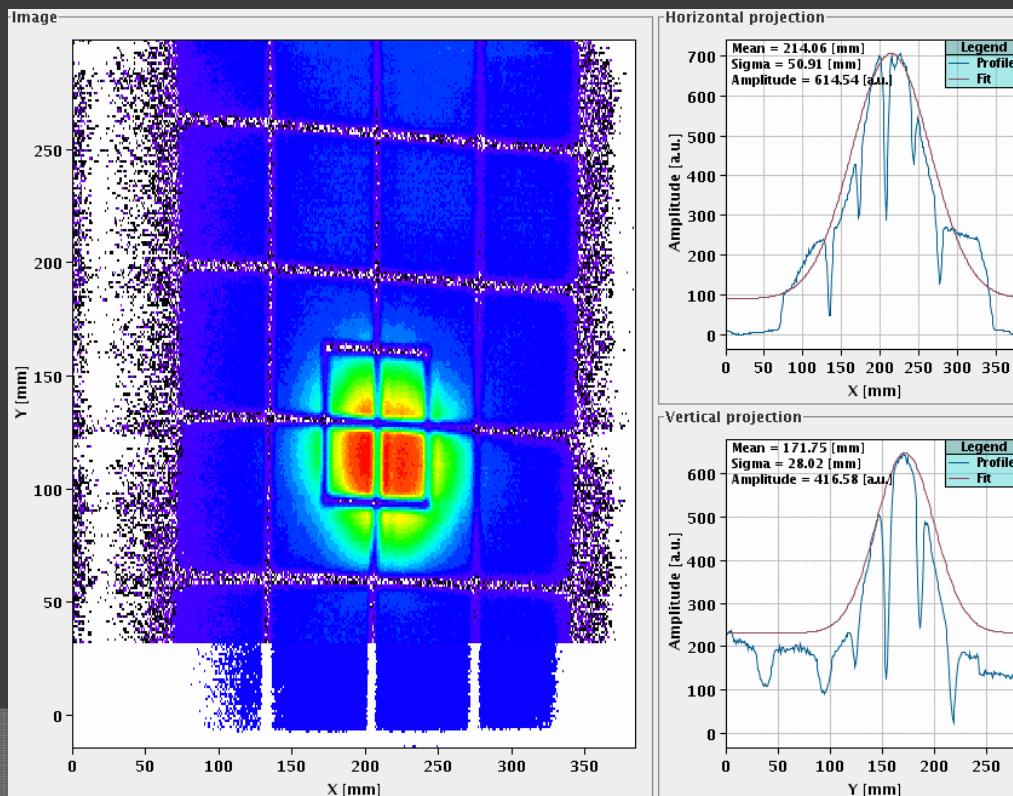


Access 28th Aug. 07

Hardware installation on beam line completed

- Door D201 installed (EA and TS/CSE)
- Access system modified (TS/CSE)
- Cryogenics installed
- Optical diagnostics adjusted (solenoid hoisted)



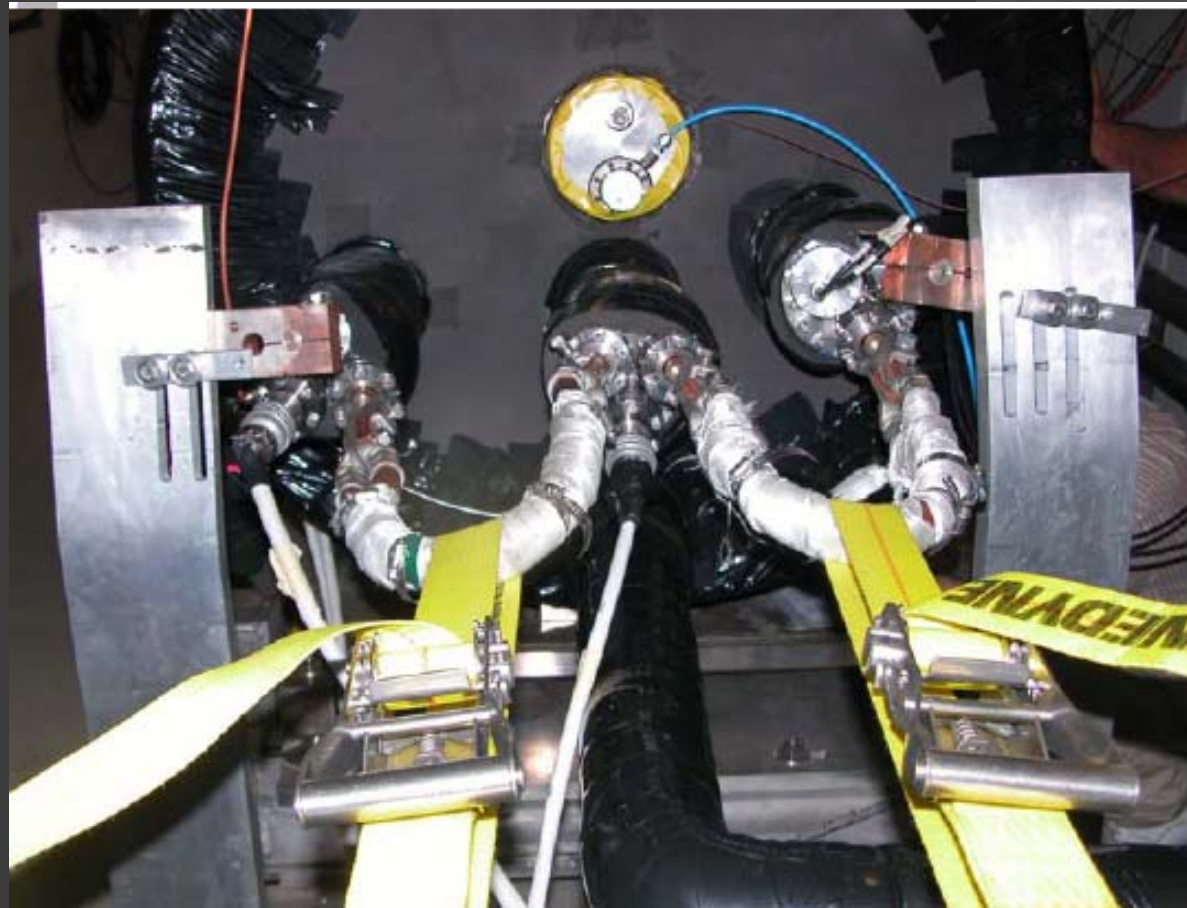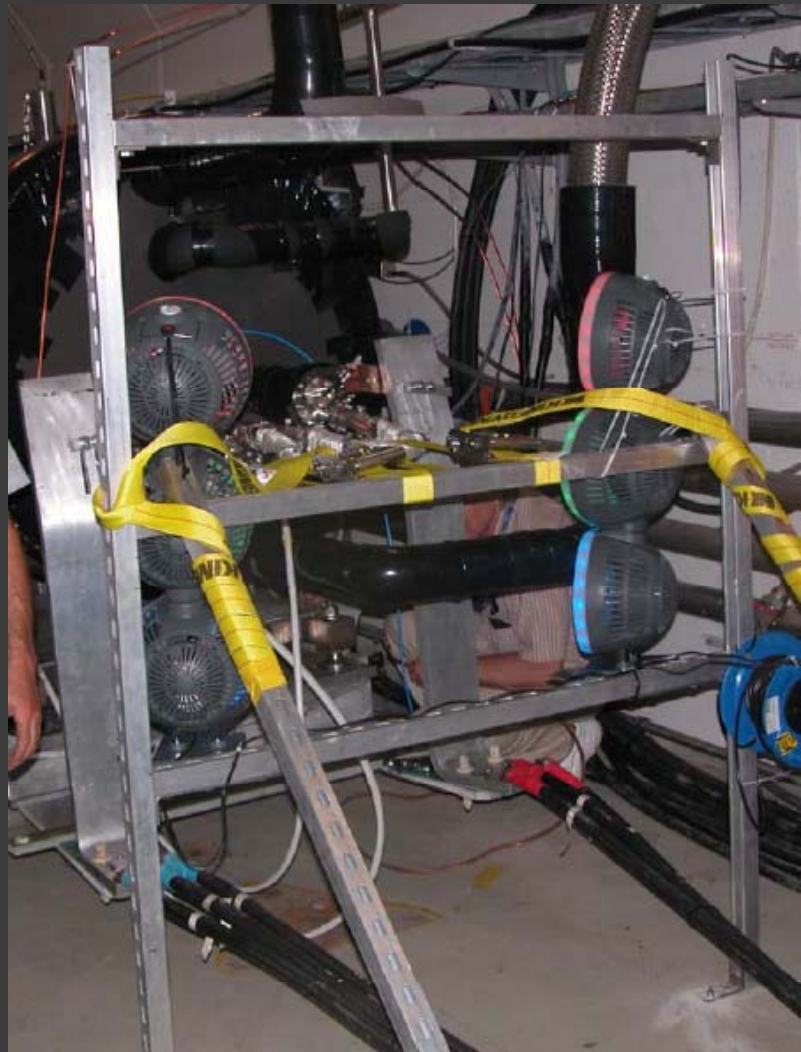

Schedule

- ⦿ September 07
 - Install Cryo installation at surface
 - Beam tuning
 - Commission power supply
- ⦿ October 07
 - Commission cryogenics
 - Commission MERIT with low intensity beam
- ⦿ End October – November 07: MERIT physics run
- ⦿ Shutdown 07/08
 - remove MERIT
 - Reinstall NToF
